

Modernization

Santa Cruz High School


Spring 2003



Are We There Yet?

(Oh, never mind)

Students are wondering, "When will the jungle gym be finished?" That "jungle gym" between the gym and library buildings is actually a custom-made, three-story elevator tower and bridge structure that will provide students improved access to the lower campus. Construction of the tower itself is nearing completion, and the installation of the rough electrical and plumbing lines are in their final stages. The structural steel deck for the bridge structure connects the gym with other campus buildings. In the next couple of weeks, the elevator subcontractor will be installing the inner workings of the elevator.

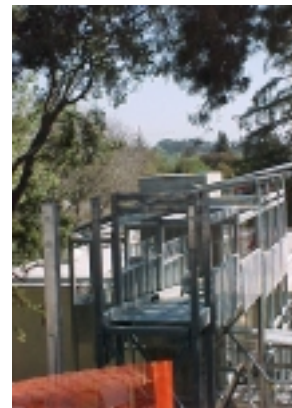

Bridge structure



The new Jungle Gym?

The sound of music can once again be heard coming from the music building. The entire building has received new flooring and paint. Some practice rooms were enlarged to accommodate larger ensembles. New ceiling tiles were installed to enhance the acoustics of the music rooms. Electrical, telecommunication, fire alarm and security systems have been upgraded. New windows have been installed throughout the entire building.



Music Building

Work is complete in the classrooms on the southeast side of the math building. Classrooms received new flooring, paint and ceiling tiles where needed. Student bathrooms have been completely redone with new partitions, fixtures and ceramic tile on the walls and floors. Similar work is under way in the classrooms on the northwest side of the building. In addition, new windows are being installed throughout the entire building. Math classes will continue to be held in the portable classrooms to mitigate any distractions due to the construction of the elevator tower and bridge structure.

Bond Oversight Committee:

Laurie Bair
Steven Barisof
Doug Cook
Matt Farrell
Dr. Jim Logsdon
Judy McGooden
William L. May
Bill Maxfield
Ann Pomper
B. Clark Stamper
Robert Thornton

District Administration:

Superintendent
Keith Parkhurst
Asst. Superintendent
Dick Moss



<http://www.sccs.santacruz.k12.ca.us/bizservices/BondProject/bondproject.htm>

Over spring break, new flooring with wood trim accents was installed in the student cafeteria and dining area. The wall and ceiling finishes have been redone. Windows have been replaced throughout this building as well. Upgrades to the electrical, telecommunication, fire alarm and security systems were expanded in this building also.

The boys and girls locker and team rooms are nearing completion. Numerous modifications to the original design have prolonged the renovation schedule. Students will soon enjoy more private yet spacious changing and shower rooms. Finishes in all of the toilet and shower rooms have been completely redone. New lockers and benches have been installed. For the first time ever, the SCHS girls varsity teams will have their own team room. The ceiling in the gym has been repaired and painted.

The mud in the quad gets deeper as the construction team wrestles with the Division of the State Architect for its approval of modifications to the foundation layouts and placement of the structural steel columns.

Selective demolition has begun in the library. The bookcases have been removed to allow for the installation of new flooring. The circulation counter has been redesigned and a new reference desk, book reader and turnstile will be installed. Ceiling tiles will be replaced as needed and the walls and ceilings will be painted. The exterior deck on the east side of the building will be removed and replaced by a new deck, providing students with a relaxing, natural study environment.

If it seems like the modernization project is taking longer than anyone expected, that's because it has. A large amount of work was added to an already ambitious scope, and most of the work had to be performed while school was in session. Nearly every building on campus has had more extensive renovation work than originally planned.

***Hang on...
we're almost there!***



Varsity Girls Team Room



Painting of Gym ceiling



Work resumes in the Quad

Project Team

Owner

Santa Cruz City Schools
2931 Mission Street
Santa Cruz, CA 95060
(831) 429-3904
Construction
Project Coordinator:
Mike Morehouse

Santa Cruz High School
415 Walnut Street
Santa Cruz, CA 95060
(831) 429-3960
Principal:
Ralph Porras

Architect

Beverly Prior Architects
375 Fremont Street, Suite 300
San Francisco, CA 94105
(415) 777-9422 Main Office
(831) 457-2940 Site Office
Project and Operation
Manager:
George Wilson
Project Manager:
Mark Hallock
Construction Coordinator:
Joanne McAlpine

Project Inspector

Construction Inspections
100 Ogier Avenue
Morgan Hill, CA 95037
(831) 423-8748 Site Office
(831) 423-8748 Fax
Inspector of Record:
Keith Woods

General Contractor

West Coast Contractors, Inc.
2320 Courage Drive, #111
Fairfield, CA 94533-6743
(707) 435-1000 Main Office
(707) 435-1010 Fax
(831) 423-8674 Site Office
Project Manager:
Marco Velasco
Project Superintendents:
Perry Herrera

Project Manager

Strategic Construction
Management
350 Coral Street, Suite E
Santa Cruz, CA 95060
(831) 466-2777
(831) 466-2776 Fax
Project Director:
David Tanza
Project Manager:
Tom Armstrong
Construction
Administration Manager:
Phyllis Christensen

Construction Budget Summary

Original Contract Amount	\$6,890,000.00
Additional Costs	\$1,803,953.00
Total Cost to Date	\$8,693,953.00
