

## Santa Cruz High School

Winter 2003



### *Historic Renovation Presents Its Challenges*

**W**hen it comes to life's more important lessons, like patience and flexibility, the students at Santa Cruz High get straight A's. Welcome to Renovation 101!

Similar lessons are being learned by West Coast Contractors Inc. Unexpected complications have delayed the drilling of the columns for the outdoor pavilion in the quad. WCC expected to find underground utilities in the quad, but instead found a tangled mess of conduits. To complicate matters, the usual means of tracing utility lines were ineffective due to the high water table. So WCC dug trenches by hand and have now identified nearly every water, gas and electric line and have rerouted those that obstructed the drilling. The quad, expected to be completed by May will provide students with a comfortable setting for outdoor dining, performances and events.

Construction of the elevator tower and bridge is progressing. The third platform of this three-story custom-built elevator is formed and poured. In the next couple weeks the roof structure will also be formed and cast in concrete. Soon afterward, the steel that will form the bridge structure will be arriving on campus and erected. The elevator tower and bridge structure, expected to be complete by June, will provide better access for the disabled.

Computer classes have resumed in the Trident Building. The computer labs now have raised flooring for future flexibility, new cabinetry, and all-new interior finishes. State-of-the-art fiber optic cabling has been installed, which will provide students with faster network and internet access.

Now that the administrative and counseling offices have moved back in to their newly renovated office spaces, work is

#### **Bond Oversight Committee:**

Laurie Bair  
Steven Barisof  
Doug Cook  
Matt Farrell  
Dr. Jim Logsdon  
Judy McGooden  
William L. May  
Bill Maxfield  
Ann Pomper  
B. Clark Stamper  
Robert Thornton

#### **District**

**Administration:**  
Superintendent  
Keith Parkhurst  
Asst. Superintendent  
Dick Moss




underway in the music building. New ceiling tiles are being replaced as needed to improve the acoustic properties of practice rooms. Some practice rooms are being enlarged to facilitate larger ensembles. The entire building will receive new flooring, paint and an enhanced data and electrical network.

Construction continues in the locker rooms. Both the boys and girls locker and team rooms being redone with new lockers, benches, toilet-shower facilities and paint. Completion of the locker rooms is scheduled for April.

Work is ongoing in the math building. As classrooms are able to rotate into the temporary portable classrooms on campus, work will proceed there, as well as in the home economics building.

Construction Budget Summary	
Original Contract Amount	\$6,890,000.00
Additional Costs	\$1,350,662.00
Total Cost to Date	\$8,240,662.00

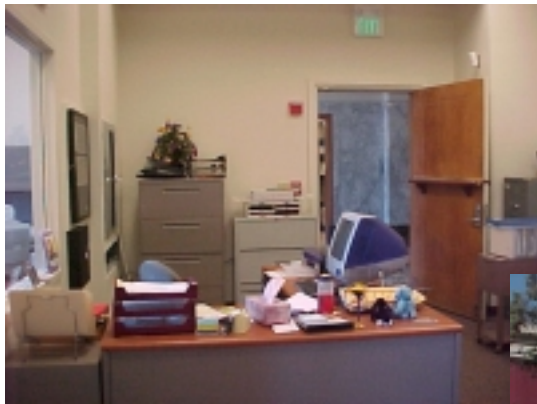

*Administration office*



*Drilling of columns in the quad*



*Construction of elevator tower*



*Main ramp*

**Project Team**

**Owner**

Santa Cruz City Schools  
 2931 Mission Street  
 Santa Cruz, CA 95060  
 (831) 429-3904  
 Construction  
 Project Coordinator:  
 Mike Morehouse

Santa Cruz High School  
 415 Walnut Street  
 Santa Cruz, CA 95060  
 (831) 429-3960  
 Principal:  
 Ralph Porras

**Architect**

Beverly Prior Architects  
 375 Fremont Street  
 Suite 300  
 San Francisco, CA 94105  
 (415) 777-9422 Main Office  
 (831) 457-2940 Site Office  
 Project and Operation  
 Manager:  
 George Wilson  
 Project Manager:  
 Mark Hallock

**Project Inspector**

Construction Inspections  
 100 Ogier Avenue  
 Morgan Hill, CA 95037  
 (831) 423-8748 Site Office  
 (831) 423-8748 Fax  
 Inspector of Record:  
 Keith Woods

**General Contractor**

West Coast Contractors, Inc.  
 2320 Courage Drive, #111  
 Fairfield, CA 94533-6743  
 (707) 435-1000 Main Office  
 (707) 435-1010 Fax  
 (831) 423-8674 Site Office  
 Project Manager:  
 Marco Valasco  
 Project Superintendents:  
 Perry Herrera  
 Jim Farmer

**Project Manager**

Strategic Construction  
 Management  
 350 Coral Street, Suite E  
 Santa Cruz, CA 95060  
 (831) 466-2777  
 (831) 466-2776 Fax  
 Project Director:  
 David Tanza  
 Project Manager:  
 Tom Armstrong  
 Construction  
 Administration Manager:  
 Phyllis Christensen
